


I-85/SR 400 Connector Ramps
 NH-85-2(153), PI No. 762380
 Fulton County

ID	Task Name	Duration	Start	Finish	Predecessors
1	Notice to Proceed	1 day	Mon 10/1/07	Mon 10/1/07	
2	Concept Development	324 days	Mon 10/22/07	Thu 1/15/09	
3	Kick-off Meeting with GDOT	0 days	Mon 10/22/07	Mon 10/22/07	
4	Project Team Kick-off	0 days	Mon 11/5/07	Mon 11/5/07	
5	Begin Aerial Mapping and Photo Control	45 days	Mon 11/5/07	Fri 1/4/08	4
6	Submit a Project Management Plan	15 days	Mon 11/5/07	Fri 11/23/07	4
7	Submit a Quality Control Plan	15 days	Mon 11/5/07	Fri 11/23/07	4
8	Perform Traffic Counts	45 days	Mon 11/12/07	Fri 1/11/08	
9	Conduct Travel Time Run	20 days	Mon 12/3/07	Fri 12/28/07	
10	Deliver Electronic Traffic Data Report to GDOT	5 days	Mon 1/14/08	Fri 1/18/08	8
11	Project Future Traffic	20 days	Thu 1/3/08	Wed 1/30/08	8FS-7 days
12	OEL Review and Approval Traffic Projections	15 days	Thu 1/31/08	Wed 2/20/08	11
13	Perform Highway Capacity Analysis	10 days	Thu 2/14/08	Wed 2/27/08	12FS-5 days
14	Conduct Micro-Simulations	45 days	Thu 2/14/08	Wed 4/16/08	12FS-5 days
15	Alternative Assessment	15 days	Thu 5/29/08	Wed 6/18/08	50,14
16	Initial Concept Team Meeting	0 days	Wed 6/18/08	Wed 6/18/08	15
17	Develop Concept Layouts	100 days	Thu 2/28/08	Wed 7/16/08	
18	Freeway Guide Sign Concept	10 days	Thu 7/17/08	Wed 7/30/08	17
19	TrueViz Animation	129 days	Mon 2/4/08	Thu 7/31/08	
20	Prepare a Project Design Data Book	108 days	Mon 3/3/08	Wed 7/30/08	
21	Prepare Cost Estimates	5 days	Thu 7/17/08	Wed 7/23/08	17
22	Prepare Draft Concept Report	15 days	Thu 7/24/08	Wed 8/13/08	21
23	Schedule and Hold Concept Team Meeting	1 day	Thu 8/14/08	Thu 8/14/08	22
24	Compile and Distribute Concept Team Meeting Minutes	10 days	Fri 8/15/08	Thu 8/28/08	23
25	Revise Concept Layout and Draft Concept Report	15 days	Fri 8/29/08	Thu 9/18/08	24
26	Provide GDOT with information to conduct a VE Study	5 days	Fri 9/19/08	Thu 9/25/08	25
27	Attend the VE meetings	5 days	Fri 9/26/08	Thu 10/2/08	26
28	Respond to all VE comments	10 days	Fri 10/3/08	Thu 10/16/08	27
29	Revise Concept & Report to Incorporate VE Comments	15 days	Fri 10/17/08	Thu 11/6/08	28
30	Submit a Final Concept Report	0 days	Thu 11/6/08	Thu 11/6/08	29
31	Concept Approved	15 days	Fri 11/7/08	Thu 11/27/08	30
32	Prepare Displays and Fact Sheet for PIOH	15 days	Fri 11/28/08	Thu 12/18/08	31
33	Attend PIOH Dry Run	0 days	Thu 12/18/08	Thu 12/18/08	32
34	Hold Public Information Open House (PIOH)	0 days	Thu 12/18/08	Thu 12/18/08	33
35	Assist GDOT investigate questions & comments from PIOH	5 days	Fri 12/19/08	Thu 12/25/08	34
36	Draft written responses for all comments received at PIOH	5 days	Fri 12/26/08	Thu 1/1/09	35
37	Revise Concept & Report to Incorporate PIOH Comments	10 days	Fri 1/2/09	Thu 1/15/09	36
38	Final Concept	0 days	Thu 1/15/09	Thu 1/15/09	37
39	Draft IMR	45 days	Thu 6/19/08	Wed 8/20/08	15
40	IMR Review and Comments (GDOT and FHWA)	40 days	Thu 8/21/08	Wed 10/15/08	39
41	Final IMR	20 days	Thu 10/16/08	Wed 11/12/08	40
42	Develop Alignments & Cross Sections to Support EA	15 days	Fri 11/7/08	Thu 11/27/08	30
43	PM2.5 Determination Letter	30 days	Fri 11/7/08	Thu 12/18/08	29
44					
45					

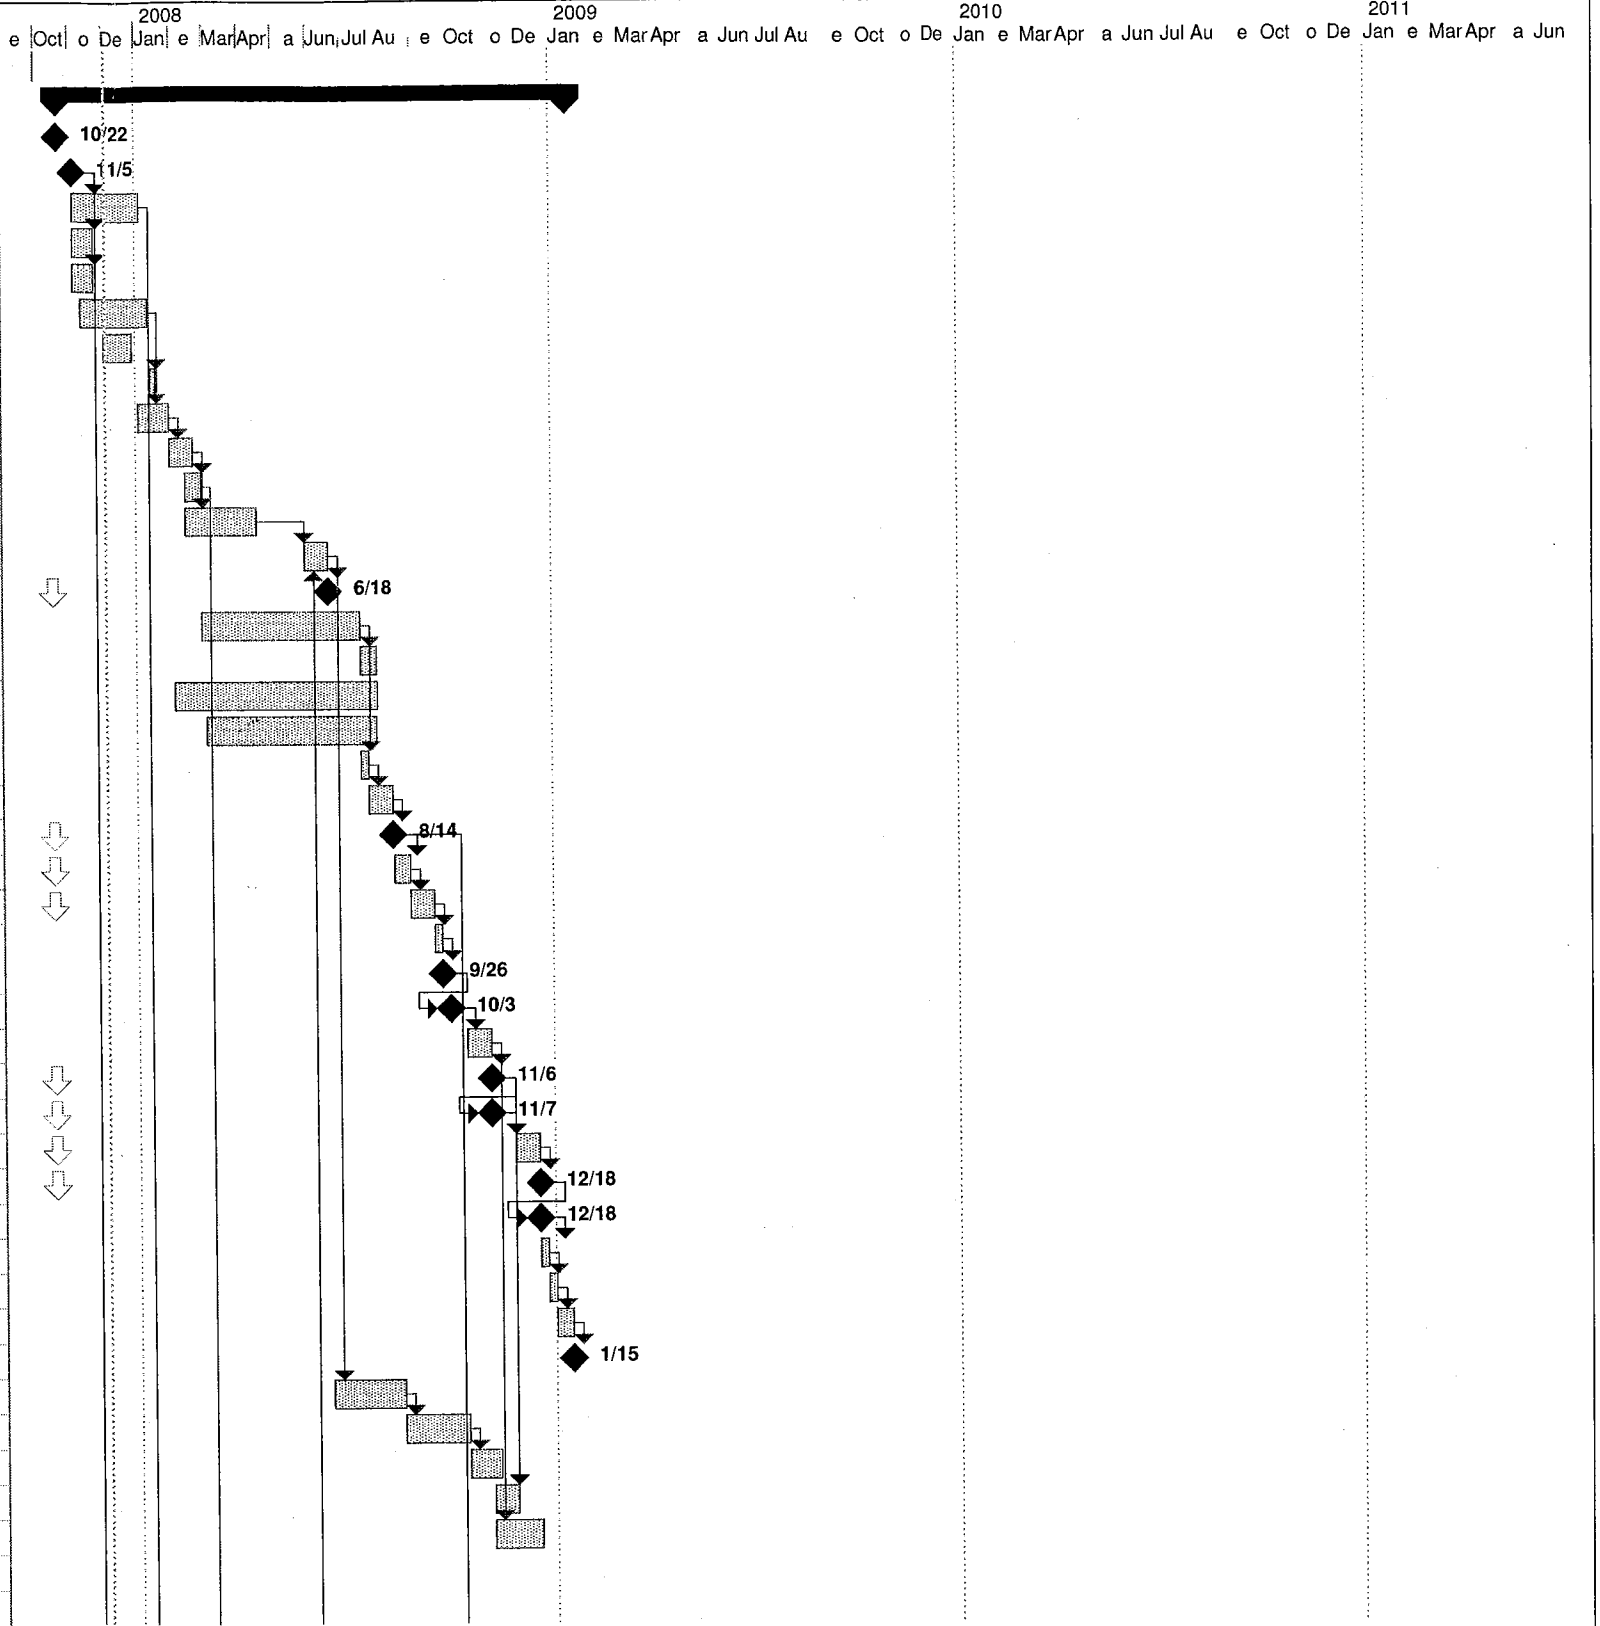

Project: Project Workplan for Concept
 Date: Mon 12/3/07

Task: [Pattern] Progress
 Split: [Pattern] Milestone


Summary: [Pattern] Summary
 Project Summary: [Pattern] Project Summary

External Tasks: [Pattern] External Tasks
 External Milestone: [Pattern] External Milestone

Deadline: [Pattern] Deadline

I-85/SR 400 Connector Ramps
 NH-85-2(153), PI No. 762380
 Fulton County

ID	Task Name	Duration	Start	Finish	Predecessors
46	Environmental Document	555 days	Mon 11/5/07	Fri 12/18/09	
47	Begin Historic Resource Field Investigation	45 days	Mon 11/5/07	Fri 1/4/08	4
48	Begin Ecology Field Work	45 days	Mon 11/5/07	Fri 1/4/08	4
49	Begin Special Studies	40 days	Thu 2/28/08	Wed 4/23/08	13
50	Identify & Resolve Environmental Issues and Constraints	25 days	Thu 4/24/08	Wed 5/28/08	49,47,48
51	Submit History and Ecology Reports	0 days	Wed 5/28/08	Wed 5/28/08	50
52	Prepare PAR Report and Hold Field Investigation	60 days	Thu 5/29/08	Wed 8/20/08	51
53	NEPA Document Preparation	90 days	Thu 8/21/08	Wed 12/24/08	52
54	Submit Draft EA	0 days	Wed 12/24/08	Wed 12/24/08	53
55	GDOT Review	20 days	Thu 12/25/08	Wed 1/21/09	54
56	Revise Draft EA	30 days	Thu 1/22/09	Wed 3/4/09	55
57	FHWA Review	40 days	Thu 3/5/09	Wed 4/29/09	56
58	Revisions to EA	17 days	Thu 4/30/09	Fri 5/22/09	57
59	Draft Approval	0 days	Fri 5/22/09	Fri 5/22/09	58
60	Circulate Draft EA to Resource Agencies for Comment	60 days	Mon 5/25/09	Fri 8/14/09	59
61	Public Hearing	0 days	Fri 8/14/09	Fri 8/14/09	60
62	Prepare Final EA	60 days	Mon 8/17/09	Fri 11/6/09	61
63	Submit Final EA	0 days	Fri 11/6/09	Fri 11/6/09	62
64	FHWA Review	30 days	Mon 11/9/09	Fri 12/18/09	63
65	FONSI Approved	0 days	Fri 12/18/09	Fri 12/18/09	64
66	Database	300 days	Mon 1/7/08	Fri 2/27/09	
67	Develop Property Database	30 days	Mon 1/7/08	Fri 2/15/08	5
68	Survey Obscure Areas	30 days	Mon 10/13/08	Fri 11/21/08	23,67
69	Complete Survey Database	60 days	Mon 12/8/08	Fri 2/27/09	68
70					
71	Preliminary Plans	275 days	Mon 12/29/08	Fri 1/15/10	
72	Preparation	175 days	Mon 12/29/08	Fri 8/28/09	
73	Review/Revisions	45 days	Mon 8/31/09	Fri 10/30/09	72
74	Submit Plans for PFPR	10 days	Mon 11/2/09	Fri 11/13/09	73
75	PFPR & Report Approval	45 days	Mon 11/16/09	Fri 1/15/10	74
76					
77	Right of Way Plans	333 days	Mon 11/2/09	Wed 2/9/11	
78	Preparation	42 days	Mon 11/2/09	Tue 12/29/09	
79	Review/Revisions	35 days	Wed 12/30/09	Tue 2/16/10	78
80	Approval	20 days	Wed 2/17/10	Tue 3/16/10	79
81	R/W Acquisition	236 days	Wed 3/17/10	Wed 2/9/11	80
82					
83	Final Plans	354 days	Fri 1/15/10	Wed 5/25/11	
84	Preparation	157 days	Fri 1/15/10	Mon 8/23/10	
85	Review/Revisions	20 days	Tue 8/24/10	Mon 9/20/10	84
86	Submit Plans for FFPR	10 days	Tue 9/21/10	Mon 10/4/10	85
87	FFPR & Report Approval	45 days	Tue 10/5/10	Mon 12/6/10	86
88	Final Submittal	79 days	Tue 12/7/10	Fri 3/25/11	87
89	Letting (GDOT)	43 days	Mon 3/28/11	Wed 5/25/11	88

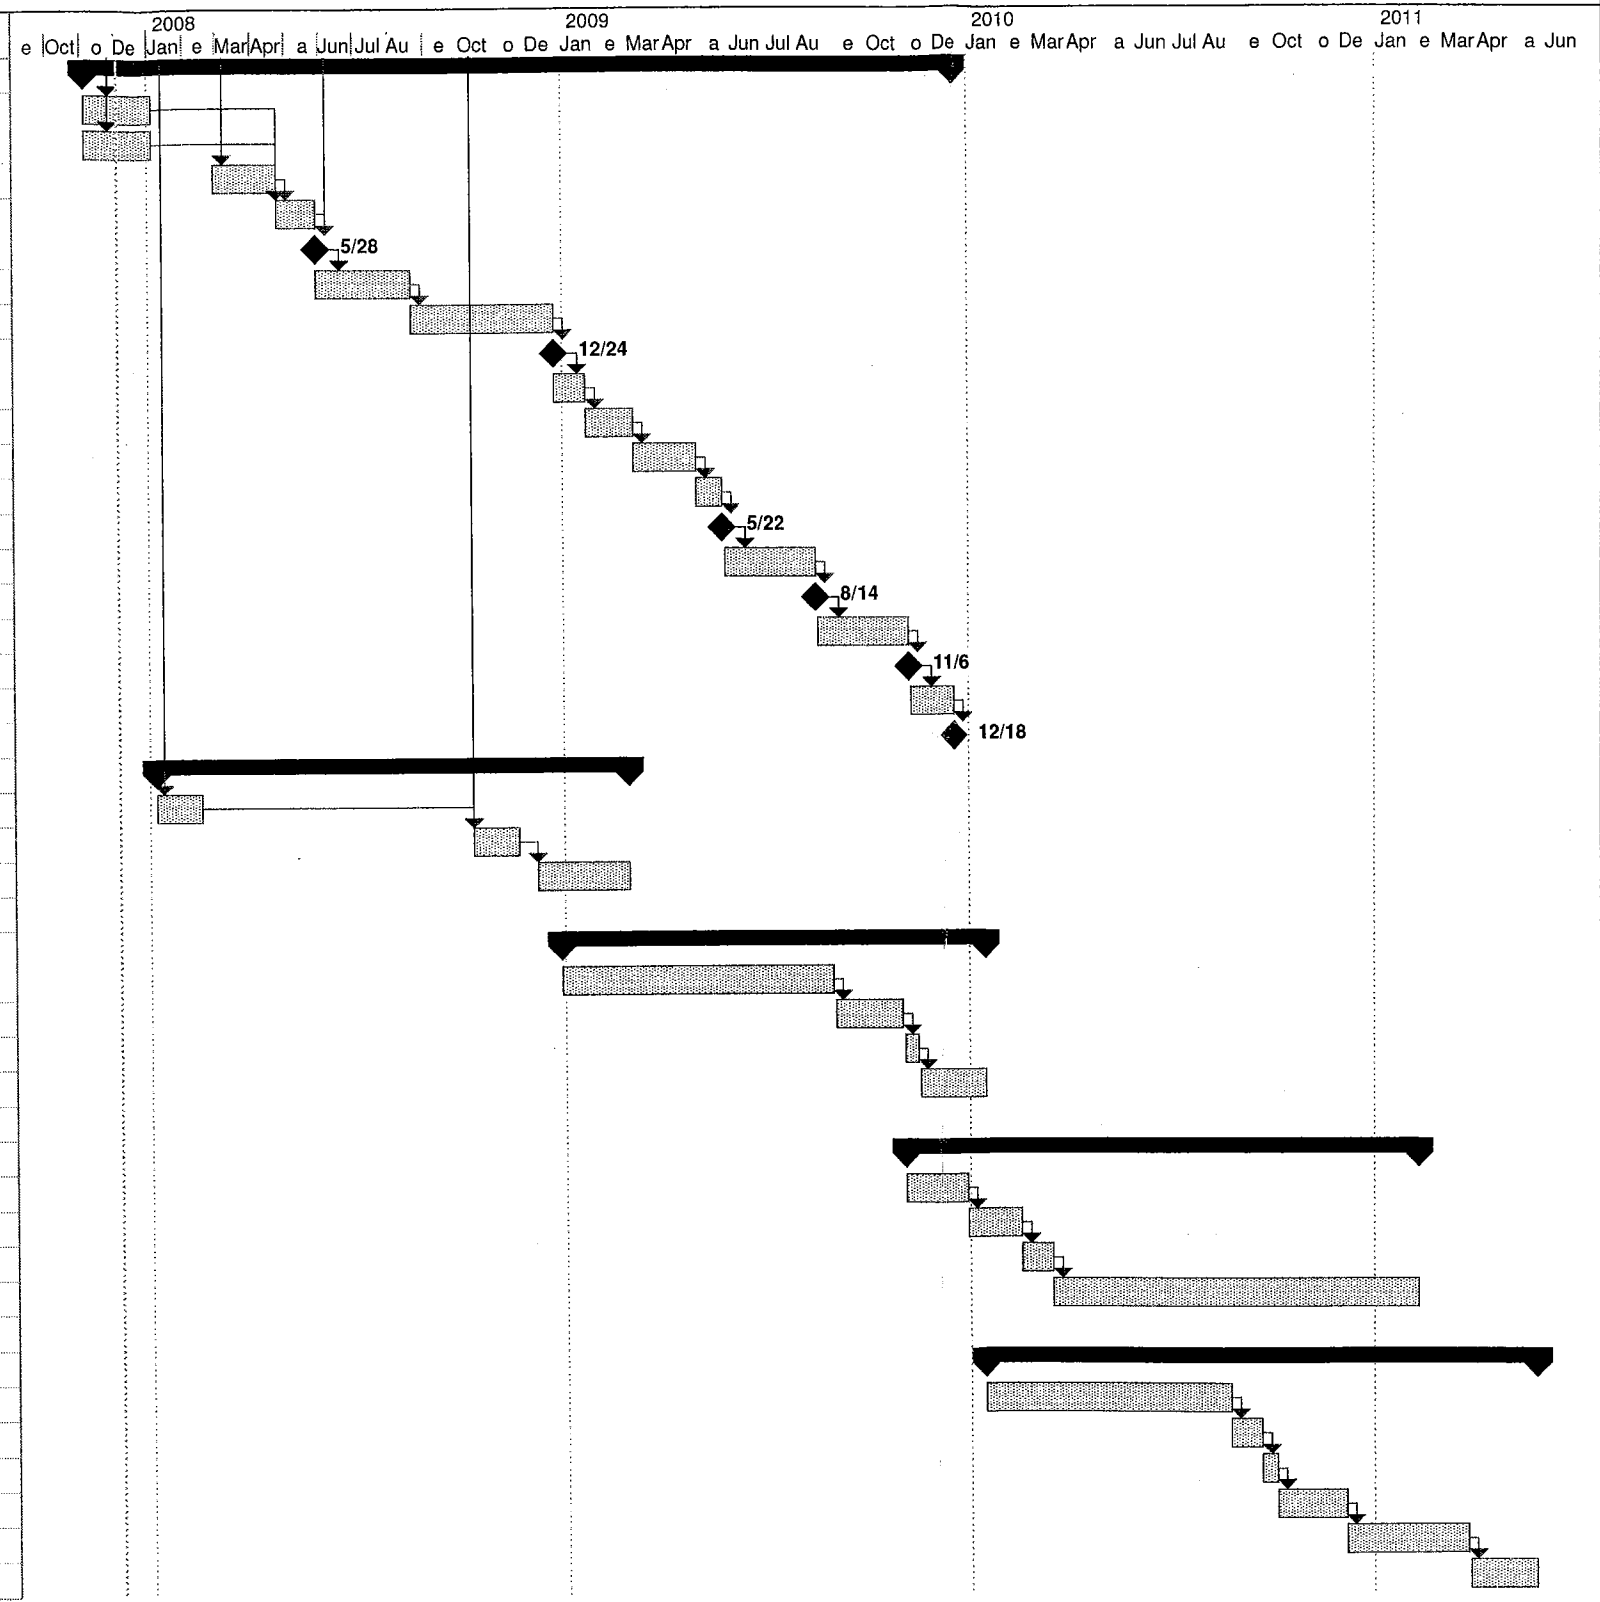

Project: Project Workplan for Concept
 Date: Mon 12/3/07

Task		Progress		Summary		External Tasks		Deadline
Split		Milestone		Project Summary		External Milestone		
